



Casalduni 34.7 MW Wind Farm, Campania, Italy

Parco Eolico Casalduni House S.r.l.

Contact



Fichtner Italia S.r.l.
Via XII Ottobre 2/41
16121 Genova

Foro Bonaparte 55
20121 Milano

www.fichtner.de/en/



Francesco Gennaro

+39 010 5956 902 ext 209
francesco.gennaro@fichtner.it

Fichtner Italia Srl



Simone Prato

+39 010 5956 902
simone.prato@fichtner.it

Fichtner Italia Srl

Document approval

	Name	Signature	Position	Date
Prepared by:	S. Prato M. Canevello		Consultant Engineers	23.11.2021
Checked by:	F. Gennaro		Project Manager	24.11.2021

Document revision record

Rev.	Date	Details of revision	Fichtner Doc Ref.	Prepared by	Checked by
0	11.2021	Rev. 0	RP 21 191_F454	Fichtner Italia	Fichtner Italia

Disclaimer

This document has been prepared by Fichtner within the framework of a Contract which defines the scope and use of such document as well as the responsibilities borne by Fichtner with respect to the information contained therein. The distribution of this document to different parties and/or the application of the document or of the information contained therein to a different scope or use as provided for in the Contract is forbidden and Fichtner shall not be responsible for such other scope or use. Should the documents be even partially modified, the use of the Fichtner logo, formats and letterheads is prohibited.

Note

Unless differently stated, this Report has been prepared on the basis of the information gathered and/or project documents reviewed up to the cut-off date of October 31, 2021.

Table of Contents

1	Executive Summary	5
2	Background	8
3	Introduction	9
4	Contractual structure.....	10
4.1	Project Organizational Chart.....	11
5	Overall Project schedule	12
6	Project Progress	15
7	Budget.....	16
8	Permitting and Lands rights	18
8.1	Permitting	18
8.2	Lands rights.....	18
9	HSE	19
10	Site Visit	20
11	Other Pictures.....	21
	Key References.....	24
	Abbreviations	26

1 Executive Summary

This construction report covers the period of October 2021 (the "Reference Period") and provides information on the status of the main construction activities, based on the documents made available by the Project Company on November 16, 2021.

Overall Progress

Due to a landslide on the SS90, Km 48 + 500 that prevent the WTGs from following the originally planned route the works have faced a small delay compared to the initial schedule. SGRE has found an alternative route (starting from the Barletta port, in Apulia) in order to plan the delivery of WTGs to the construction site.

ANAS Campobasso got in touch with the transporter providing its list of infrastructures to be included in the technical report that the technician of SGRE and the transport company will have to provide.

ANAS provided the transportation conditions on the SS645 from km 28+740 to km 1+070, SS710 from km 2+450 to km 0+000 and SS87 from km 131+800 to km 105+850 [23].

As so far, in accordance with the main activities planned at the beginning of the works are related to the following:

- The Executive Project of the Electrical Substation was completed, as also foundations' design was finalized. It is foreseen to deposit the Executive Project to Genio Civile within July 2021.
- UXO test (Unexploded Ordinances): both the first and the second partial explosive ordinance clearance testing were obtained.
- Archaeological surveys: archaeological assistance with the University of Salerno and other archaeologists will be started along with the start of activities expected to be in the end of May/early July 2021 [3]; birdlife monitoring activities have been contracted.
- Foundations: Seismic authorization obtained for 8 WTGs. The additional documents required by the *Genio Civile* for WTG03 and WTG18 have been conducted in April, and the seismic authorisation was obtained on May 4, 2021 [3]. As regards the Substation, the deposit of seismic authorization was carried out.

Moreover, it has been stipulated a contract with Siemens for the electromechanical supply. In relation to contracts, the Client foreseen to sign contracts with the suppliers for the following materials/works:

- Supply MV and F.O. cables (Nexans)
- Supply and laying HV cables
- Supply Concrete – Plinth and Piles
- Supply Additives – Foundations
- Supply Cave dry materials (signed)
- Subcontract earth moving (signed)
- Subcontract Treatment at lime
- Subcontract Piles (signed)
- Subcontract Carpenter (signed)
- Subcontract prefabricated cabins in SS (signed)

The TA notifies that, based on the updated project schedule, the Updated Interconnection Date Deadline (April 20, 2022) as per definition in the Waiver of Terms and Conditions of the Notes dated October 4, 2021, meet the project requirements.

Moreover, the TA notes that, based on the updated project schedule, the Long Stop Date (July 31, 2022) as per definition in Terms and Conditions of the Notes would be met just 5 days in advance (July 26, 2022), subject to a hypothetical obtainment of WTG transport permit on November 30, 2021, which is yet to be confirmed by the involved authorities.

However, the current schedule would allow the Project to be guaranteed the awarded Tariff without any penalties: the deadline to avoid a 1% reduction on the awarded Tariff for the projects awarded in third auction (in accordance with the DM July 4, 2019), whose ranking results were published in September 2020, was extended to October 31, 2022 due to the current COVID-19 emergency [9].

The TA notes that the buffer to meet this target (represented by the date of energization of the first WTG, currently foreseen for April 20, 2022) is quite large, and safe also in case of further delays.

Budget

No. 5 WTG EXW (batch 2) as per the EPC contract payment milestones have been occurred in the Reference Period.

The costs are related to the advance payment EPC occurred in July 2019 and the WTG Contract/SSE Contract stipulated in December 2020, as well as the Cable Supply Contract in February 2021 and the 5 WTG EXW milestone of November 2021, for a total amount of 32,441.6 k€.

Permitting and Land acquisition/concession

- The land rights were obtained on August 1, 2020. The payment for the land costs related to the landowners and MEF are in final phase (90% of the payment has been conducted). The remaining part is expected to be finalized before the starting of the works;
- The land rights for provisional areas are foreseen to be completed by the end of July based on the works progress in the construction site;
- First and second UXO (Unexploded Ordinances) with positive result obtained.
- Seismic authorization obtained for 8 WTGs upon to 10 WTGs. The additional documents required by the Genio Civile for the seismic authorization for WTG18 and WTG03 have been obtained on May 4, 2021.
- It has been stipulated the concession with the Province of Benevento for the laying of the cable duct obtained on July 17, 2020 and the authorization for roads adjustment on February 5, 2021.;
- The authorisation for the cable duct line was obtained from the Pontelandolfo Municipality on April 15, 2021. No related concession will be issued, as it is not needed¹.
- The authorization from the Casalduni Municipality for the cable duct is still pending;
- The ANAS authorization for roads adjustment was obtained on March 29, 2021
- Decree of EIA Extension was obtained March 23, 2021 with positive comments from MATTM and MIBACT. Within July the MITE (former MATTM) is expected to comply with the Decree of EIA Extension. After the compliance, site works will be initiated;

¹ Confirmed by Renexia with clarification email on 28/05/2021

- ANAS consent for new route obtained on November 16, 2021.

HSE

Safety and Coordination Plan were issued in the Reference Period [1].

Site Visit

To be planned in accordance with new time schedule / progress of site activities. Considering the start of works within the end of November, the site visit is envisaged to be performed in the vicinity of that date.

2 Background

The Casalduni WF (the "Project" or the "Wind Farm"), with a total capacity of 34.7 MW consisting of 10 Siemens-Gamesa G132-3.465MW with a hub height of 114 m, received the EIA Decree on November 22, 2014 and has been authorized by the Campania Region according to the D.Lgs. 387/2003 ("Autorizzazione Unica" or "AU") on March 22, 2016. On November 27, 2019 by the AU Decree n.465, the Campania Region issued the Single Authorization for the Project as "Variante".

The Wind Farm is owned by Parco Eolico Casalduni House Srl (the "Project Company" or the "PC" or the "Client"), which in turn is owned by Renexia SpA (the "Sponsor").

In the 2018, Fichtner has been mandated for the lender's engineering activities for the benefit of each financial institution providing debt service to the Project Company according to their individual needs.

As informed by the Sponsor, the Project applied to the third auction in accordance with the DM July 4, 2019. The auction ranking results were published in September 2020. The Project was awarded a tariff of 66.84 €/MWh, corresponding to a 4.51% discount with respect to the threshold tariff of 70 €/MWh, assigned for 20 years starting from the Project COD.

In this framework new turbine supply and O&M contracts (TSA and ISP) have been signed with the Danish WTG manufacturer Siemens Gamesa on December 2020.

Fichtner Italia ("Fichtner" or the "TA" or "LE"), mandated as lender's engineer, has been requested to provide a Construction Report related to the update status of the Project.

During this exercise, the TA has liaised with, or received information from, representatives of the following parties:

- Parco Eolico Casalduni House (PECH) as SPV;
- Renexia as Sponsor

3 Introduction

This report aims to provide the Lenders with the status of the main project construction activities for the Reference Period.

The works mainly consist of:

- Building and installation of 10 WTGs composed by 9 deep foundations (piles) and 1 foundation that transfers the load directly on the terrain, for a total installed power of 34.65 MW;
- Execution of the MV cable-ducts;
- Construction of the SSE for the MV/HV transformation of the produced energy;
- Construction of the HV cable duct connected with the RTN² line.

All the WTGs are located in Municipality of Casalduni, grouped into two clusters: WTG03, WTG04 and WTG05 belonging to the first cluster and the WTG08, WTG09, WTG10, WTG11, WTG13, WTG14 and WTG18 are in second cluster, while the SSE is located in the Municipality of Pontelandolfo, nearly the existing substation RTN.



Figure 3-1 – Layout of all WTGs and SSE

² "Rete elettrica di Trasmissione Nazionale", High Voltage Transmission Line

4 Contractual structure

The Project foresees a contractual structure, summarized in the following figure and table:

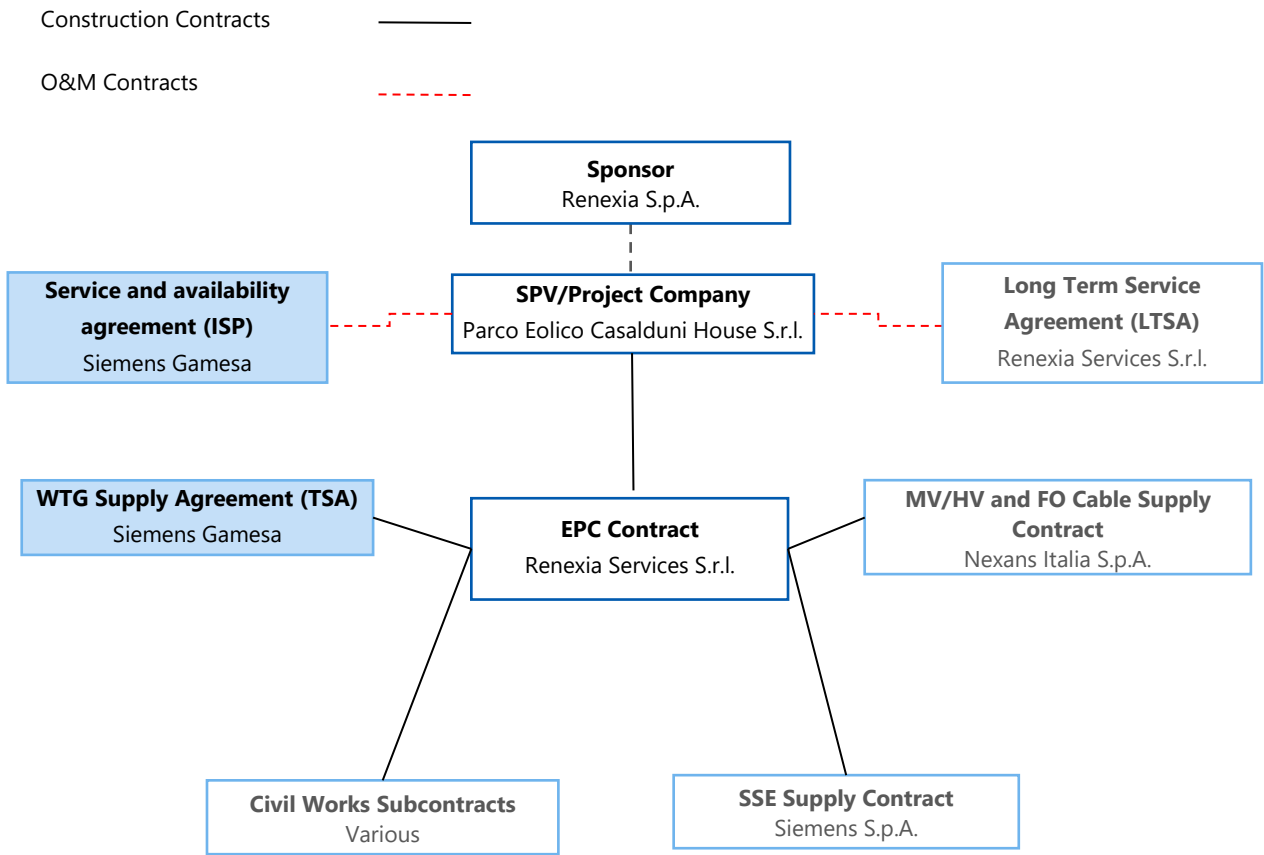


Table 4-1: Casalduni WTG Project Contracts

The new contractual scheme technically covers all the main activities related to the procurement, construction/erection/installation and testing of the Project. This structure will expose the EPC contractor to risks coming from their direct involvement on several responsibilities pertaining to transportation and WTG’s towers supply and installation/testing.

4.1 Project Organizational Chart

The EPC Contractor Renexia Services S.r.l. has shared the following Organizational Chart highlighting the main roles and responsibilities of its resources during the Project execution:

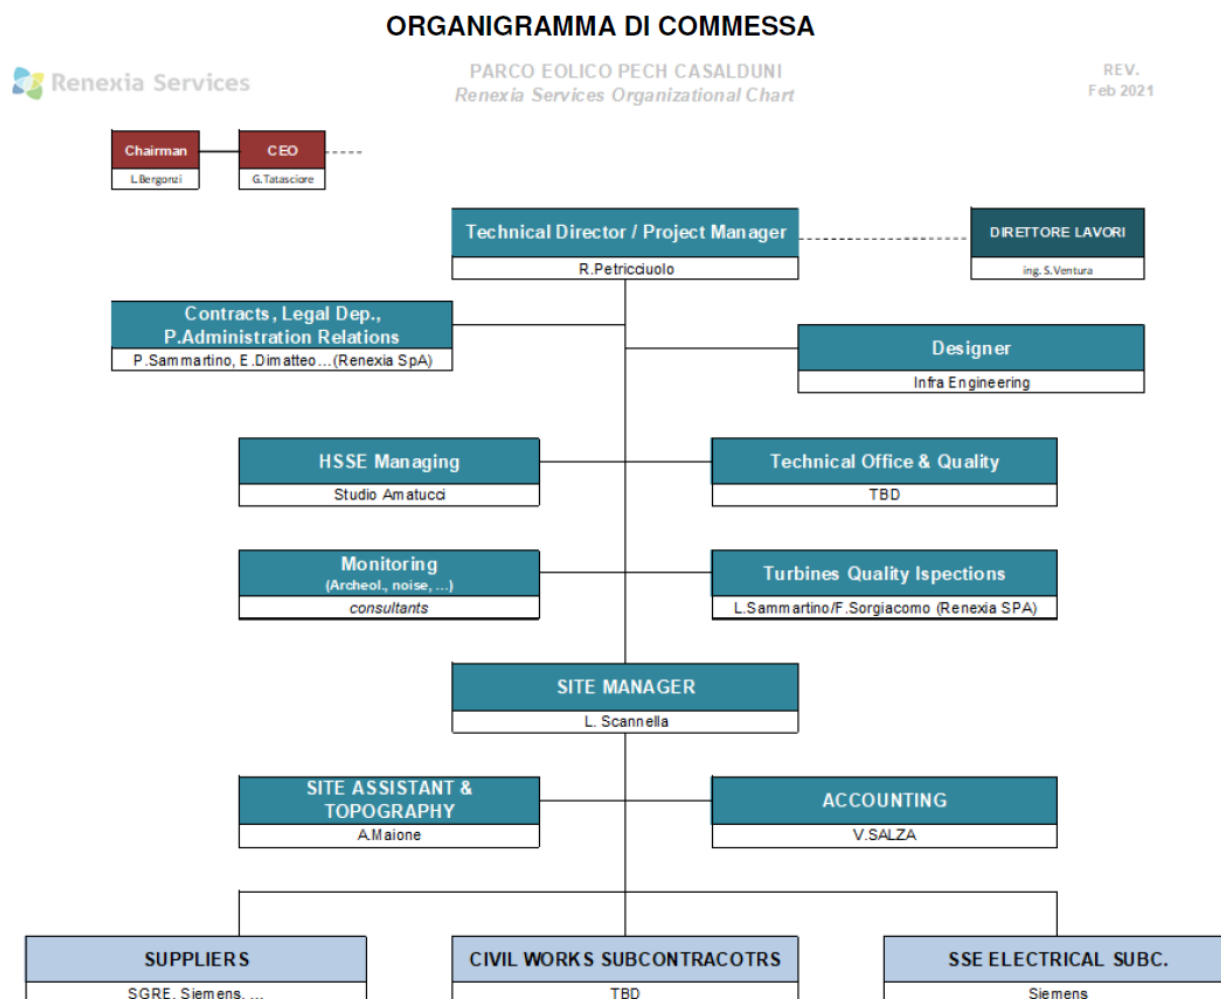


Table 4-2: Project Organizational Chart of EPC Contractor

This organisational structure is, in the TA's opinion, aligned with the industry standard.

5 Overall Project schedule

The dates of the construction milestones are reported in the overall project schedule of the Wind Farm provided to the TA at DD phase compared with the new timetable to be attached to the EPC amendment [2]:

Event	Planned Schedule [2]	Updated Schedule Sept 21 [17]	Update Schedule and TA's comments
Construction Contracts	Done	Done	The Notice to Proceed (NTP) signed in the mid of January 2021 between the EPC contract and the TSA (Siemens Gamesa).
UXO Survey	Partially Done	Done	
Start of Site Works	In the mid of May	November 30, 2021 [Delay 3 months]	<p>After the obtainment of the Decree <i>Proroga VIA</i> on March 23, 2021. Renexia stated that Site Works will start at the end of July.</p> <p>The delay is due, according to Renexia, to a landslide on the SS90, Km 48 + 500 that stopped the delivery of materials by the manufacturer SGRE after contacts and meetings on November 16, 2021 ANAS sent the transportation conditions report on the SS645 from km 28+740 to km 1+070, SS710 from km 2+450 to km 0+000 and SS87 from km 131+800 to km 105+850 [23].</p> <p>As informed by the Sponsor [25], SAE company (sub-contractor SGRE for the transportation), is currently dialogue with ANAS Campobasso. They already provided a first survey of the infrastructures present along the route and awaits communication from ANAS of any laboratory checks to be carried out on some of the bridges along the route.</p>
WTGs delivery on site	From 09/09/2021 to 15/12/2021	From January to April 2022. ³ [Delay: 4 months]	<p>The WTG blades have arrived in the Naples port according to the schedule [1].</p> <p>Since the installation envisages a "Just-in-time" approach, the transportation is planned at the delivery on site of the whole set of the main components at the end of the WTG's foundations.</p>

³ Confirmed by Renexia via mail on 29/07/21

			See previous note for information on final site delivery.
MV Cables delivery on site	31/03/2021	From December 2021 to January 2022 [Delay: 5 months]	The MV Cable delivery on site is foreseen until January 2022, a delay of 5 months is observed on this procurement item, due to the delay on WTG delivery. On this regard, the Sponsor informed that manufacturing of MV cables is complete in June, and the MV cables are available at manufacturer's facilities [1].
HV Cables delivery on site	1/09/2021	January 2022 [Delay: 4 months]	The MV Cable delivery on site is foreseen until January 2022, a delay of 5 months is observed on this procurement item, due to the delay on WTG delivery.
WTGs foundation completion	6/10/2021	February 2022 [Delay: 4 months]	The activity has been postponed due to delay in WTG delivery, as typically foundation completion and WTG installation are performed in sequence to optimize costs and logistics of the involved companies.
20/150kV SSE Energization	10/11/2021	From April 11 to 19, 2022 [Delay:4 months]	The energization of the Electrical Substation is foreseen in April 2022.
MV Cables and F.O: installation	From to 13/05/2021 to 27/10/2021	June 2022 [Delay: 8 months]	Carried out by Nexans Italia S.r.l. Due to delay in WTG delivery, in analogy with WTG foundation completion.
WTGs Erection	15/12/2021	From January to April 2022 [Delay:4 months]	The erection of all WTGs will be completed on April 11, 2022.
Mechanical Completion WTGs	From 14/10/2021 to 19/01/2022	May 2022 [Delay:4 months]	Due to delay in WTG delivery.
WTGs Energization	From 16/12/2021 to 26/01/2022	May 2022 [Delay:4 months]	According to the new schedule, the first WTG Energisation will occur on April 20, 2022
WTGs trial tests	From 27/01/2022 to 23/03/2022	June 2022 [Delay: 3 months]	The test run of the WTGs will be completed at the end of June 2022.

WTGs Take Over	From 17/03/2022 to 20/04/2022	July 2022 [Delay: 3 months]	The WTGs Take Over is foreseen to be finalized on July 19, 2022
Wind Farm Take Over	27/04/2022	July 2022 [Delay: 3 months]	The TO is foreseen to be on July 26, 2022 and will be achieved following the final inspection.

For the transportation topic, based on the available documentation, the alternative route appears feasible even though around 100 km longer than the original one. This might entail an increase in WTG transportation cost, which however the TA estimates as a minor drawback and anyway on the EPC contractor responsibility.

The Sponsor informed that, in order to demonstrate route feasibility and delivery of all components to each installation location, additional inspection and testing is required prior to the start of transportation. As a matter of fact, ANAS Campobasso got in touch with the transporter [21] at the beginning of October (slightly outside the relevant period of the present report but reported during its preparation), providing its list of infrastructures to be included in the technical report that the technician of SGRE and the transport company (SAE) will have to provide.

Risk low | #1 In accordance with the timeline previously described ANAS provided the transportation conditions on the SS645 from km 28+740 to km 1+070, SS710 from km 2+450 to km 0+000 and SS87 from km 131+800 to km 105+850 [23]. As informed by the Sponsor [25], SAE is currently dialogue with ANAS Campobasso providing a first survey of the infrastructures present along the route and awaits communication from ANAS of any laboratory checks to be carried out on some of the bridges along the route.

6 Project Progress

The activities carried out so far can be summarized as follows:

- Completion of WTG executive design and seismic deposit. Ex Works of 10 WTGs out of 10
- Anchor bolts and blades delivered on site;
- UXO testing carried out and certificates obtained

In the Reference Period (October 2021):

- Executive design of User SS carried out, deposit in progress;
- WTG blades arrived in the port of Napoli;
- Siemens materials (nacelles, hub and tower) are stored in Spain waiting to be shipped to the port of Barletta;
- Auxiliary transformer FAT successfully passed ;
- Main HV/MV transformer FAT successfully passed (see also Section 11);
- Transport authorization to be finally received.

7 Budget

The incurred construction costs amount, based on the EPC Contract milestones, are reported in the table below, as per the latest version of the Schedule, updated in November 2021 [24].

Month	SAL [k€]	%	Milestone
Milestones achieved			
4 July 2019	10,954.3	26.0%	Advance payment EPC
Oct-19	-	0.0%	
Nov-19	-	0.0%	
Dec-19	-	0.0%	
FY19	10,954.3	26.0%	
Jul-20	-	0.0%	
Aug-20	-	0.0%	
Sep-20	-	0.0%	
Oct-20	-	0.0%	
Nov-20	-	0.0%	
Dec-20	1,053.3	2.5%	WTG Contract/SSE Contract
FY20	1,053.3	2.5%	
Jan-21	-	0.0%	
Feb-21	632.0	1.5%	Cable Supply Contract
Jun-21	842.6	2.0%	Cables EXW
Jun-21	2,527.9	6.0%	Site Delivery Anchor bolts
Jul-21	-	0.0%	
Aug-21	8,426.4	20.0%	No. 5WTG EXW batch 1
Nov-21	8,005.1	19.0%	No. 5WTG EXW batch 2
Milestones not yet achieved			
Nov-21	1,264.0	3.0%	Transformer EXW
FY21	21698.0	51.5%	
Jan-22	842.6	2.0%	Cables delivery on site
Apr-22	1,264.0	3.0%	WTG Foundation completed – MW Cable and FO installation completed
Jun-22	1,264.0	3.0%	SSE Energization/Mechanical completion
Jun-22	842.6	2.0%	Definitive Platform and Roads completed
Jul-22	4,213.2	10.0%	Provisional Acceptance Certificate
FY22	8,426.4	20.0%	

Tabella 7-1: EPC Contract Milestones status

No. 5 WTG EXW (batch 2) as per the EPC contract payment milestones have been occurred in the Reference Period (see LT 21 260_F454 - Casalduni WF_n.07 Draw Down Certificate dated November 3, 2021).

8 Permitting and Lands rights

An updated status of the authorization process and events occurred in the Reference Period, related to permits and land rights, is provided in the following, based on the information provided by the PC report [1].

8.1 Permitting

The first partial testing BOB (UXO-unexploded ordinance) was obtained with issuance of the report of partial validation number 34 on January 25, 2021.

For the small areas occupied by SSE and WTG04 and the municipality roads, the submission of the request for second partial UXO test was carried out, and the UXO test was executed on May 20, 2021 [1], followed by the issuance of the report of partial validation number 226 on May 24, 2021.

The Seismic Authorization for the 8 WTGs were obtained, excepted for the WTG03 and WTG08, whose additional documents required by the Genio Civile have been delivered. The related authorization has been obtained by Genio Civile on May 3, 2021 [10]. Instead, the seismic authorization for the substation were deposited. The documentation about executive design of SS is complete. The deposit to Genio Civile is foreseen within October (due to some delay in signature obtainment).

The obtainment of the EIA Decree of *Proroga* was on date March 24, 2021 [7], which acquired the positive opinions from the EIA commission of the MATTM and MIBACT. Within July the MITE (former MATTM) is expected to comply with the Decree of EIA Extension. After the compliance, site works will be initiated

8.2 Lands rights

The private parcels affected by the project were acquired through notary agreements already in August 2020. The payments related to the lands of the owners and/or deposit to MEF are at the phase of conclusion (90% of the payment done). The remaining part is expected to be finalized before the starting of the works. A detailed and updated report of the payments will be shared later by Renexia [3].

The land rights for provisional areas – mainly relative to the access of exceptional transport carriers - are foreseen to be completed between May-June, based on the works progress in the construction site, in order not to impact major site activities [3].

Province of Benevento: the concessions for cable duct installation were obtained on July 17, 2020 [8] and the related works for external roads adjustment on February 5, 2021 [5]

Pontelandolfo Municipality: the authorization for laying the cable duct was obtained on April 15, 2021 [4].

Casalduni Municipality: the authorization for the cable duct line is awaited [3].

ANAS: the authorization for the adjustment of external roads was obtained on March 29, 2021 [6], except for a minor intervention at Buonalbergo, whose authorization is awaited shortly according to Renexia [1]. SGRE obtained the necessary transport authorizations (see Section 5).

9 HSE

No Safety and Coordination Plan has been issued in the Reference Period [1].

10 Site Visit

To be planned in accordance with new time schedule / progress of site activities. Considering the start of works within the end of November, the site visit is envisaged to be performed in the vicinity of that date.

11 Other Pictures

In the following, some pictures of the arrival of the WTG blades in the port of Naples, shared by the Sponsor, are attached [1]:



Figure 11-1 - WTG Blades at the port of Naples

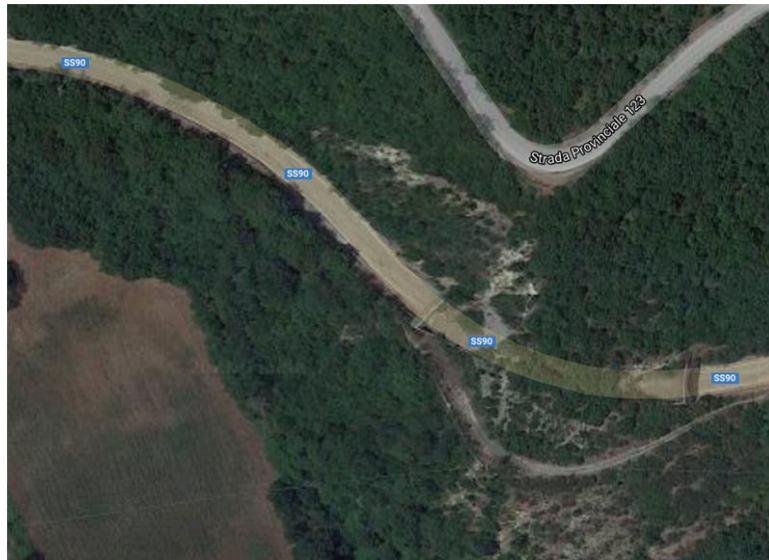


Figure 11-2 - Landslide on SS 90

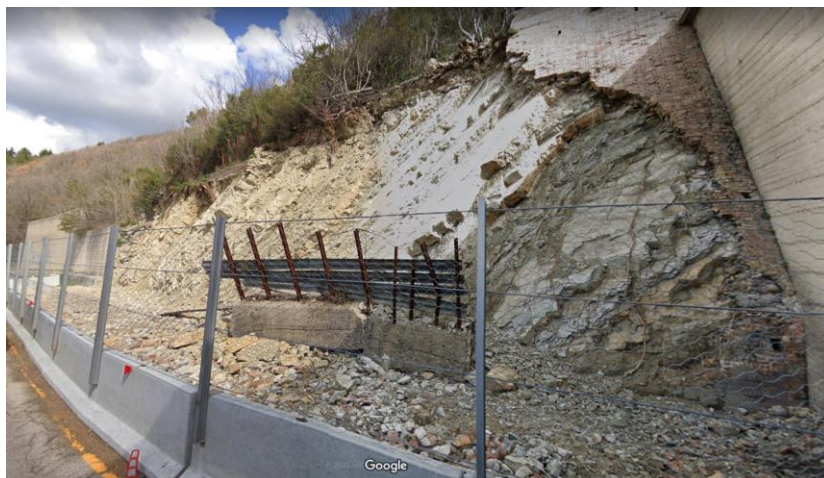


Figure 11-3 - Landslide on SS 90



Figure 11-4 - transformer qualification

Key References

Doc. Ref.	Title	File Name	Version / Date
1	Construction Report	211029_report costruzione Casalduni.pdf	Received on November 16, 2021
2	Time schedule	Renexia Services P.E.C.H. – Programme nov2020.pdf	February 23, 2021
3	Clarifications	Email 22.05.2021	May 22, 2021
4	Pontelandolfo Municipality Concession	Prot_Par 0003131 del 13-04-2021 - Documento CCF_000073.pdf	April 23, 2021
5	Province Benevento for roads adjustment concession	concessione 21 del 05022021 SP95.pdf concessione 22 del 05022021 SP87.pdf	April 23, 2021
6	ANAS authorization for roads adjustment	220882.pdf 220892.pdf	April 23, 2021
7	EIA Decree Proroga	ID_VIP_4993_Parere_SCVIA_n_128 (1).pdf MATTM_2020-0094513 (1).pdf	April 23, 2021
8	Province Benevento for cable duct line concession	UFFICIALE.2020.0017445_disciplinare.pdf p_bn.REGISTRO UFFICIALE.2020.0017474_disciplinare.pdf p_bn.REGISTRO UFFICIALE.2020.0017314_disciplinare.pdf	April 23, 2021
9	Extension of the deadline for the application of the 1% reduction of the tariff referred to in Article 7.3.a for plants registered in a useful position in the rankings formed pursuant to the third auction	Delibera Consiglio dei Ministri 31/01/2020, Delibera Consiglio dei Ministri 29/07/2020, Delibera Consiglio dei Ministri del 07/10/2020, Delibera Consiglio dei Ministri del 13/01/2021	January 13, 2021
10	Seismic authorisation for WTG03 and WTG08, issued by Genio Civile	NOTA PROT. N. 241414 DEL 04-05-2021_AutSism_3-18	May 4, 2021
11	SS works schedule by Siemens Energy	Programma Lavori elettromeccanici	June 15, 2021
12	Client's plan of SS works by Siemens Energy	Piano Della Committenza rev.00	June 15, 2021
13	Acceptance of Payment Schedule Amendment	FRAME - Amendment to the EPC Agreement (Acceptance)	July 14, 2021

Doc. Ref.	Title	File Name	Version / Date
14	Drawdown Certificate form Milestones "Cables EXW" and "Site Delivery Anchor Bolts"	LT 21 198.1_F454 - Casalduni WF_n.05 Draw Down Certificate_rev.1-signed	June 16, 2021
15	Amended Payment Schedule, July 2021	PECH_EPC milestone curve_july21_TP	July 14, 2021
16	SGRE EXW Certificate - WTG Blades	Exhibit E_Delivery Certificate Blades	June 30, 2021
17	Project Schedule updated, August 2021	Renexia Services P.E.C.H.- Programme Sept2021 REV1	August 31, 2021
18	Casalduni Draw-down certificate #6 - Milestone certificates and other attachments	LT 21 229_F454 - Annex 2	June-July 2021
19	Casalduni Draw-down certificate #6	LT 21 229_F454 - Casalduni WF_n.06 Draw Down Certificate-signed	August 6, 2021
20	Alternative road survey by WTG transportation company	ROAD SURVEY (CB) - CASALDUNI WIND FARM	September 27, 2021
21	ANAS communication to WTG transporter	ANAS CB - Richiesta Relazione Tecnica	October 11, 2021
22	5 WTG EXW milestone certificate	Milestone certificate_202109	September 2, 2021
23	Clarification email 18.11.2021	Email from Renexia dated 18.11.2021	November 18, 2021
24	Project Schedule updated, October 2021	211029_report costruzione Casalduni.pdf	October 29, 2021
25	Renexia clarifications	Email received by Renexia's Technical Director	November 24, 2021

Abbreviations

BOP	Balance of Plant
CAPEX	Capital Expenditures
COD	Commercial Operation Date
EXW	EX Works (<i>Franco Fabbrica</i>)
HV	High Voltage
IEC	International Electrotechnical Commission
kW	Kilowatt
kWh	Kilowatt-hour
LD	Liquidated Damage
LV	Low Voltage
MCR	Major Components Replacement
MLA	Mandated Lead Arranger
MP	Monopile
MW	Megawatt (1,000 kW)
MWh	Megawatt-hour (1,000 kWh)
MV	Medium Voltage
O&M	Operation and Maintenance
PC	Project Company
SCADA	Supervision Control and Data Acquisition
TA	Technical Advisor
TOC	Take Over Certificate
VAT	Value Added Tax
WF	Wind Farm
WTG	Wind Turbine Generator
